



MINISTRY OF DEFENCE NEGARA BRUNEI DARUSSALAM

QUOTATION FOR

**DISMANTLING WORKS, TRANSPORTING AND INSTALLATION OF
THREE (3) UNITS PORTABLE CABINS AT JABATAN KASTAM DAN
EKSAIS DIRAJA (JKED) BUILDING, SUNGAI TUJOH TO CONTROL
KG BEBULOH, KAMPUNG JUNJONGAN AND KAMPUNG LUMAPAS**

**QUOTATION NO : JPPK / SH / 05 / 2026 – 2027
(MINDEF/DFA/FY2026/ITAU/Q/008-BOL)**

CLOSING DATE : 29 – 10 – 2026

CLASS : III and above

CATEGORY : KA01 AND B01

QUOTATION SUBMISSION

**QUOTATION BOX NO: 5 (DFA)
ARAS BAWAH
BANGUNAN ARKIB
KEMENTERIAN PERTAHANAN
BOLKIAH GARRISON BB3510
NEGARA BRUNEI DARUSSALAM**



**MINISTRY OF DEFENCE
NEGARA BRUNEI DARUSSALAM**

SUMMARY OF QUOTATION

for

**DISMANTLING WORKS, TRANSPORTING AND INSTALLATION OF
THREE (3) UNITS PORTABLE CABINS AT JABATAN KASTAM DAN
EKSAIS DIRAJA (JKED) BUILDING, SUNGAI TUJOH TO KG
BEBULOH, KAMPUNG JUNJONGAN AND KAMPUNG LUMAPAS**

**JPPK / SH / 05 / 2026 – 2027
(MINDEF/DFA/FY2026/ITAU/Q/008-BOL)**

Instruction to Tenderers

There is no quotation fee for this project. Relevant document(s) can be obtained by downloading from Ministry of Defence website at <http://www.mindef.gov.bn> and click on “Tender & Quotation” tab and go to “Quotations” box as the quotation document can be found in the provided folder with respect to its closing date.

This quotation is open to Tenderers registered as Contractors under Ministry of Development, Negara Brunei Darussalam under **Category KA01 and B01**. The Tenderer shall furnish the valid registration document stated herein prior to the submission of this quotation in order to carry out the above works.

The Tenderer is required to submit the **updated and valid** Company Registration Certificate (Form 16/17 or Form X) and Ministry of Development’s Registration Certificate together with their quotation.

Non-compliance with the conditions in any respect shall render the tender liable for rejection.

Tenderers **MUST** submit with their quotation a complete list of the following Appendices:

Appendix Description

- | | |
|---|---|
| A | LIST OF PREVIOUS JOBS EXPERIENCE OF A SIMILAR NATURE |
| B | LIST OF CURRENT JOBS IN BRUNEI |
| C | PROPOSED LIST OF JOBS TO BE SUB-CONTRACTED |
| D | INFORMATION ON THE DISTRIBUTION OF APPROVED LABOUR QUOTA |
| E | PROPOSED MANPOWER ALLOCATION AND ADDITIONAL LABOUR QUOTA REQUIRED |
| F | PROPOSED LIST OF EQUIPMENT TO BE USED FOR THIS PROJECT |
| G | SITE INSPECTION CERTIFICATE |

Articles of Agreement and Condition of Contract

The articles of agreement and conditions of contract to be incorporated into the Contract Documents for this project shall be 'CONTRACT FORM FOR MINOR WORKS' as currently practice in Governments projects within Negara Brunei Darussalam.

Scope of the Works

The main feature of the scope of works to be undertaken by the successful Tenderer is to provide everything deemed necessary such as materials, labour, plant and equipment, supervision and transportation, etc. for the proper execution of the works all in accordance with specification and bill of quantities stated herein with a satisfactory completion and operational.

All Tenderers are to liaise with the project engineer for further information prior to preparation of quotation to ascertain on the scope of works. Any ambiguities shall be referred to the Government's Representative whose decision shall be final.

Site Location and Site Visit

The location of site is within the protected area of **Jabatan Kastam dan Eksais Diraja Sg Tujoh, Kg Bebuloh, Kg Junjongan and Kg Lumapas**. Tenderer is advised to seek assistance from the **Project Engineer (+673-7172709)** for a site visit. The Tenderer shall have taken into account all relevant aspect of the works. The Government reserves the right to accept quotations only from those Tenderers who have conducted site visit.

Payment

The payment will be paid upon the completion of the works to the satisfactory of the Government all in accordance with the document.

Completion Period

The successful tenderer shall carry out and complete the works within **1 month** from the date of award.

Validity

The submitted quotation shall remain valid for six (6) calendar months from the closing date of quotation and no Tenderers may withdraw their quotation within that period.

Submission

Tenderers are to deliver **ONE (1) SET OF HARDCOPY DOCUMENT** and **ONE (1) SET OF SCANNED SOFTCOPY DOCUMENT** in **PDF** of the priced quotation documents duly completed including relevant certificates, appendices and requested information. The scanned softcopy shall be submitted in compact disc (**CD**) in the same envelope as the quotation document.

The quotation is to be lodged not later than **8:00am** to the **quotation submission address provided herein on the day and date as per stated on covering page of this quotation document** in a properly sealed envelope marked:

Quotation for:

**JPPK / SH / 05 / 2026 – 2027 (MINDEF/DFA/FY2026/ITAU/Q/008-BOL)
DISMANTLING WORKS, TRANSPORTING AND INSTALLATION OF THREE (3)
UNITS PORTABLE CABINS AT JABATAN KASTAM DAN EKSAIS DIRAJA (JKED)
BUILDING, SUNGAI TUJOH TO KG BEBULOH, KAMPUNG JUNJONGAN AND
KAMPUNG LUMAPAS**

Queries

Any queries regarding the quotation and further information can be made to:

Project Engineer

Development Section,

Directorate of Development and Work Services

Negara Brunei Darussalam

Tel: +6737172709 (H/P)



**MINISTRY OF DEFENCE
NEGARA BRUNEI DARUSSALAM**

FORM OF QUOTATION

**QUOTATION FOR : DISMANTLING WORKS, TRANSPORTING AND
INSTALLATION OF THREE (3) UNITS PORTABLE
CABINS AT JABATAN KASTAM DAN EKSAIS
DIRAJA (JKED) BUILDING, SUNGAI TUJOH TO KG
BEBULOH, KAMPUNG JUNJONGAN AND
KAMPUNG LUMAPAS**

**QUOTATIONS NO : JPPK / SH / 05 / 2026 – 2027
(MINDEF/DFA/FY2026/ITAU/Q/008-BOL)**

CLOSING DATE : 29 – 10– 2026

-
1. I/We, ... the undersigned having read the above documents and fully understood the instruction and specification regarding the above project and willing to perform and complete the works within **1 month** from the date of site possession for **a sum of:**

Total amount in words: BRUNEI DOLLARS

Total amount in figures: B\$

Company stamp:

-
2. I/We confirm that the quotation has been calculated on a firm price basis and is inclusive of all necessary allowances to adequately cover price escalation of labour, materials and all other relevant items.
3. I/We further agree that, if our quotation is accepted, I/we will execute an Agreement in the form stated in this quotation document, which will signify our willingness to so act.
4. I/We agree that this quotation remains open for consideration and acceptance for six (6) calendar months from the last date for submission of same.

5. I/We hereby agree and note the following: -

Commencement Date : Within Fourteen (14) days from the Date of the Letter of Award

Completion Date : 1 month from the Date for Possession of Site

Defects Liability Period : Six (6) months from the Date of Completion of the work

Liquidated and Ascertain Damages :
$$\frac{\text{Contract Amount} \times 15\%}{\text{No. of days of Contract}}$$

As WITNESS our hand this _____ day of _____ 2026

SIGNATURE

Signature _____ in the capacity of

_____ duly authorized to

sign tenders on behalf of _____

MOD/ PWD Class : _____

Address : _____

Witness: _____

Address : _____

Designation : _____

Company Stamp: _____

BILL OF QUANTITIES*for***DISMANTLING WORKS, TRANSPORTING AND INSTALLATION OF THREE (3) UNITS
PORTABLE CABINS AT JABATAN KASTAM DAN EKSAIS DIRAJA (JKED) BUILDING,
SUNGAI TUJOH TO KG BEBULOH, KAMPUNG JUNJONGAN AND KAMPUNG LUMAPAS**

ITEM	DESCRIPTION	UNIT	QTY	RATE (B\$)	AMOUNT (B\$)
	<u>GENERAL NOTES</u>				
	The Contractor shall arrange by themselves for visiting the site to ascertain the extent, limitation constraints and accessibility to and from site.	-	-	-	Note
	The Contractor shall allow for all cost considered necessary for the satisfactory completion of the works which shall be include:	-	-	-	Note
	i). Compliance with the requirement of preliminaries as stated in the P.W.D General Specification for Building and Construction Works	-	-	-	Note
	ii). Transportation cost throughout the course of the project duration to and from site	-	-	-	Note
	iii). Price deemed inclusive of all necessary equipment and protections for the execution of this works.	-	-	-	Note
	iv). The contractor is also required to adhere all specific requirements in carry out repair works and protection of the works. Provide three (3) full sets of postcard size progress and record photographs to the S.O or his representative before, during and after completion of the work.	-	-	-	Note
	v). The Contractor shall provide necessary precautionary measures for the workers against health hazard during alteration / repair works and is required to exercise all requirements of safety stated by Ministry of Development and MINDEF OHS regarding this matter. Precaution shall also be made not to damage any other adjoining elements and properties of the structure not for demolition works. Making good works to damage properties shall be bear at contract own cost.	-	-	-	Note
	vi). The Contractor should allow for the above items and any other related cost in the pricing of the following cost. No claim will be entertained on the Contractor's failure or ignorance of this clause.	-	-	-	Note
	vii). Rates to be included of supply all necessary materials, scaffolding, labours, tools, plant, pictures, equipment, supervision and any other essentials required for executing the project and to protect surrounding and to observe safety and cleanliness at the site and clear all debris to contractor's own dumpsite.	-	-	-	Note
	viii). Provision and compliance to HSE requirement and insurance shall be bear at contractor own cost.	-	-	-	Note

ITEM	DESCRIPTION	UNIT	QTY	RATE (B\$)	AMOUNT (B\$)
	All works shall be carried out in accordance with relevant standards, safety regulations, and the Engineer's instructions.	-	-	-	Note
1	<u>DISMANTLING, LOADING, TRANSPORTING AND UNLOADING WORKS</u>				
1.1	DISMANTLING WORKS FOR CABIN AT JKED, SUNGAI TUJOH (CONTAINER A, B AND C) Site inspection and verification of cabin conditions and services. Disconnection of all utilities including electrical, water, data/telecommunication, and sewage systems in compliance with safety regulations. Protection of reusable components and existing finishes. Careful dismantling of portable cabins, including roofing, wall panels, flooring systems, doors, windows, internal fittings, and structural supports. Labeling and systematic segregation of components for ease of reassembly. Prevention of damage to reusable materials during dismantling. Clearing and removal of debris and disposal of unwanted materials to off-site approved dumping sites. <i>(Refer to drawing APPENDIX 1 AND 2 attached)</i>		Lump Sum		
1.2	<u>LOADING AND TRANSPORTATION (CONTAINER A) TO KG BEBULOH</u> Safe loading of all dismantled components onto suitable transport vehicles. Provision of protective wrapping, packing, and securing of materials to prevent damage during transit. Transportation from Location JKED Sungai Tujoh to Control Command Post (CCP) Alpha at Kampung Bebuloh, including all logistical arrangements, permits, and handling costs.		Lump Sum		
1.3	<u>LOADING AND TRANSPORTATION (CONTAINER B) TO KG JUNJONGAN</u> Safe loading of all dismantled components onto suitable transport vehicles. Provision of protective wrapping, packing, and securing of materials to prevent damage during transit. Transportation from Location JKED Sungai Tujoh to Control Command Post (CCP) Charlie at Kampung Junjongan, including all logistical arrangements, permits, and handling costs.		Lump Sum		
CARRIED FORWARD				BS	

ITEM	DESCRIPTION	UNIT	QTY	RATE (B\$)	AMOUNT (B\$)
1.4	<u>LOADING AND TRANSPORTATION (CONTAINER C) TO KG LUMAPAS</u> Safe loading of all dismantled components onto suitable transport vehicles. Provision of protective wrapping, packing, and securing of materials to prevent damage during transit. Transportation from Location JKED Sungai Tujoh to Control Command Post (CCP) Delta at Kampung Lumapas, including all logistical arrangements, permits, and handling costs.				
1.5	<u>UNLOADING AND INSTALLATION WORKS KG BEBULOH (CONTAINER A)</u> Offloading and safe handling of materials at Location. Reassembly and installation of portable cabins in accordance with original configuration or as directed by the Engineer. Alignment, leveling, and structural securing of cabins on prepared foundations or supports. Reassemble all building components and finishes. Reassembly of electrical fittings and power supply connections as directed by Electrical Engineer. <i>(Refer to drawing APPENDIX 3 attached)</i>		Lump Sum		
1.6	<u>UNLOADING AND INSTALLATION WORKS AT JUNJONGAN (CONTAINER B)</u> Offloading and safe handling of materials at Location. Reassembly and installation of portable cabins in accordance with original configuration or as directed by the Engineer. Alignment, leveling, and structural securing of cabins on prepared foundations or supports. Reassemble all building components and finishes. Reassembly of electrical fittings and power supply connections as directed by Electrical Engineer. <i>(Refer to drawing APPENDIX 4 attached)</i>		Lump Sum		
CARRIED FORWARD				B\$	

ITEM	DESCRIPTION	UNIT	QTY	RATE (B\$)	AMOUNT (B\$)
1.7	<u>UNLOADING AND INSTALLATION WORKS</u> <u>AT KG LUMAPAS (CONTAINER C)</u> Offloading and safe handling of materials at Location. Reassembly and installation of portable cabins in accordance with original configuration or as directed by the Engineer. Alignment, leveling, and structural securing of cabins on prepared foundations or supports. Reassemble all building components and finishes. Reassembly of electrical fittings and power supply connections as directed by Electrical Engineer. <i>(Refer to drawing APPENDIX 5 attached)</i>		Lump Sum		
CARRIED FORWARD TO FINAL SUMMARY				BS	

ITEM	DESCRIPTION	UNIT	QTY	RATE (B\$)	AMOUNT (B\$)
2.0	<u>CONCRETING WORKS</u>				
2.1	<u>NEW REINFORCED CONCRETE RAFT FOOTING WITH BEAMS FOR PORTABLE CABINS AND REINFORCED CONCRETE DRIVEWAY ACCESSS (CONTAINER A, B AND C)</u> To design and construct a new reinforced concrete (G30) raft footing base and beams to portable cabins including a new reinforced concrete perimeter drain designed with reasonable skill and care and fit to purpose including all necessary works in accordance to British and Eurocode standards tender specifications. Cabins should be raised to a minimum of 200mm and constructed with r.c steps at door access. To include clearance of vegetation and ground levelling for the preparation of the reinforced concrete base and reinforced concrete driveway for access.		Lump Sum		
CARRIED FORWARD TO FINAL SUMMARY				BS	

ITEM	DESCRIPTION	UNIT	QTY	RATE (B\$)	AMOUNT (B\$)
3	<u>PROVISIONAL SUMS</u> Allow for Provisional Sum for any unforeseen works required during repairs, installation, and commissioning. The sum to be deducted or directed by the S.O. / Engineer and deducted in whole or in part if not required.	-	-	-	\$5,000.00
CARRIED FORWARD TO FINAL SUMMARY				B\$	

JPPK / SH / 05 / 2026 – 2027 (MINDEF/DFA/FY2026/ITAU/Q/008-BOL)
DISMANTLING WORKS, TRANSPORTING, INSTALLATION AND
MODIFICATION OF THREE (3) UNITS PORTABLE CABINS AT JABATAN
KASTAM DAN EKSAIS DIRAJA (JKED) BUILDING, SUNGAI TUJOH TO KG
BEBULOH, KAMPUNG JUNJONGAN AND KAMPUNG LUMAPAS

FINAL SUMMARY

ITEM	DESCRIPTION	FROM PAGE	AMOUNT (B\$)
1	DISMANTLING, LOADING, TRANSPORTING AND UNLOADING WORKS	B/3	
2	CONCRETING WORKS	B/5	
3	PROVISIONAL SUMS	B/6	
TOTAL PRICE TO FORM OF QUOTATION			B\$

.....
 CONTRACTOR SIGNATURE

.....
 CONTRACTOR CONTACT NO. (H.P)

.....
 (OFFICE)

.....
 COMPANY STAMP

.....
 DATE

APPENDICES

LIST OF PREVIOUS JOBS EXPERIENCE OF A SIMILAR NATURE

(SENARAI KERJA-KERJA YANG TERDAHULU YANG MEMPUNYAI PERSAMAAN DENGANNYA)

Pemborong hendaklah menyatakan kerja-kerja terdahulu yang telah Siap atau Sedang dalam pengendalian.

Tenderers must give details of their experience on works of a similar nature.

No.	Nama Projek (Name of Project)	Nama Kerja (Description of Work)	Harga (Value of Contract)	Kerja dimulakan (Dates Undertaken)	(Names of Employer and Architect/ Engineer Responsible)

Tandatangan Saksi:
(Signature of Witness):

Tandatangan Pemborong:
(Signature of Tenderer):

.....

.....

Tarikh:
(Date)

Tarikh:
(Date)

LIST OF CURRENT JOBS IN NEGARA BRUNEI DARUSSALAM

(SENARAI KERJA-KERJA YANG SEDANG DIBUAT DI-NEGARA BRUNEI DARUSSALAM)

No.	Nama Projek (Name of Project)	Letak (Location)	Harga (Cost)	Tarikh Siap (Date Completed)	% Kerja yang telah dibuat (% completed)

Tandatangan Saksi:
(Signature of Witness):

.....

Tarikh:
(Date)

Tandatangan Pemborong:
(Signature of Tenderer):

.....

Tarikh:
(Date)

PROPOSED LIST OF JOBS TO BE SUB-CONTRACTED

(SENARAI KERJA-KERJA YANG AKAN DI SUB-KONTRAK)

Bil. (No.)	Kerja-Kerja (Works)	Kepada (To)	Ulasan (Remarks)

Tandatangan Saksi:
(Signature of Witness):

.....

Tarikh:
(Date)

Tandatangan Pemborong:
(Signature of Tenderer):

.....

Tarikh:
(Date)

INFORMATION ON THE DISTRIBUTION OF APPROVED LABOUR QUOTA

(MAKLUMAN MENGENAI DENGAN PENGGUNAAN QUOTA BURUH)

Bil. Quota Buruh yang telah dibenarkan:
(Quota number approved)

Tarikh:
(Date of approval)

Jumlah dibenarkan:
(Total no. approved)

Senarai kerja-kerja yang sedang menggunakan Quota Buruh & jumlahnya:
(List of current jobs on approved labour quota)

Bil. (No.)	Name Projek (Name of Project)	Jumlah Tenaga Manusia (No. of quota used)
	Jumlah : (Total) :	
	Baki yang belum digunakan : (Balance of labour quota not used) :	

Tandatangan Saksi:
(Signature of Witness):

Tandatangan Pemborong:
(Signature of Tenderer):

.....

.....

Tarikh:
(Date)

Tarikh:
(Date)

Pemborong dikira memasukkan harga bagi menyediakan wang tahanan kepada Pejabat Buruh bagi pekerja-pekerja asing mereka dan tidak ada tambahan harga akan diberi bagi perkara ini.

(Tenderers are deemed to include costs of providing deposits to Labour Department for their foreign workers and no claims will be entertained on this matter).

Tarikh:
(Date)

PROPOSED LIST OF EQUIPMENT TO BE USED FOR THIS JOB (IF SUCCESSFUL)

(SENARAI PERKAKAS-PERKAKAS & KENDERAAN YANG AKAN
DIGUNAKAN UNTUK PROJEK)

Bil. No.	Jenis (Type)	Jumlah (Quantity)	Model No.	Muatan (Capacity)	Ulasan (Remark)

Tandatangan Saksi:
(Signature of Witness):

.....

Tarikh:
(Date)

Tandatangan Pemborong:
(Signature of Tenderer):

.....

Tarikh:
(Date)



CERTIFICATE OF SITE INSPECTION

In respect of the Tender for **JPPK/SH/05/2026-2027 – Dismantling Works, Transporting And Installation Of Three (3) Units Portable Cabins At Jabatan Kastam Dan Eksais Diraja (Jked) Building, Sungai Tujoh To Kg Bebuloh, Kampung Junjongan And Kampung Lumapas** between the Government of His Majesty the Sultan and Yang Di-Pertuan of Brunei Darussalam, represented by the Ministry of Defence (hereinafter referred to as the “Government”) and
 *
 (hereinafter referred to as the “Contractor”).

We, the Contractor, hereby certify, represent and warrant that we have fully inspected the site with the Government’s authorised representative, and are well aware of the existing/expected conditions and matters, which may affect the cost of the performance of the Works as required for the above Contract.

All inherent site condition reasonably foreseeable have been considered and priced accordingly in the Tender.

SITE INSPECTED BY:
CONTRACTOR

VERIFIED BY:
GOVERNMENT

.....
[Signature]

.....
[Signature]

Name:

Name:

.....

.....

Position:

Position: Engineer

Date:

Date:

.....
[Company Stamp]


.....
[DDWS Stamp]

*The Contractor’s Company name

APPENDIX 1

JPPK / SH / 05 / 2026 – 2027


Dismantling Works, Transporting And Installation Of Three (3) Units Portable Cabins At Jabatan Kastam Dan Eksais Diraja (Jked) Building, Sungai Tujoh To Kg Bebuloh, Kampung Junjongan And Kampung Lumapas

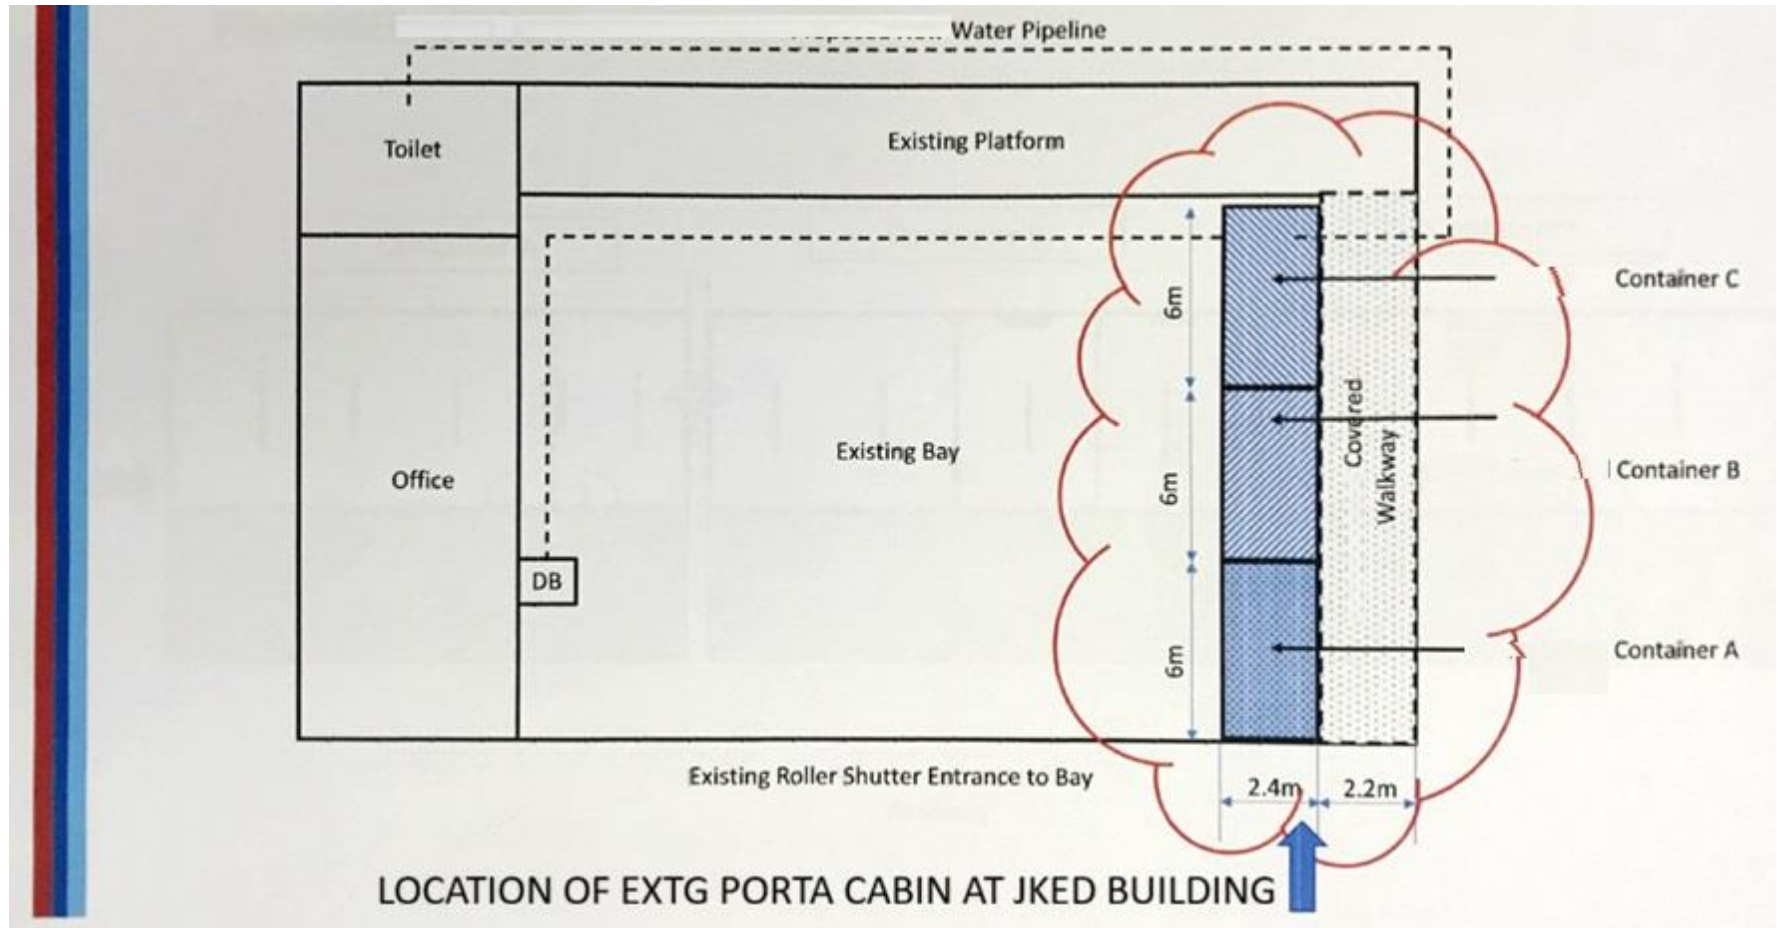

SUNGAI TUJOH

JPPK / SH / 05 / 2026 – 2027

Dismantling Works, Transporting And Installation Of Three (3) Units Portable Cabins At Jabatan Kastam Dan Eksais Diraja (Jked) Building, Sungai Tujoh To Kg Bebuloh, Kampung Junjongan And Kampung Lumapas

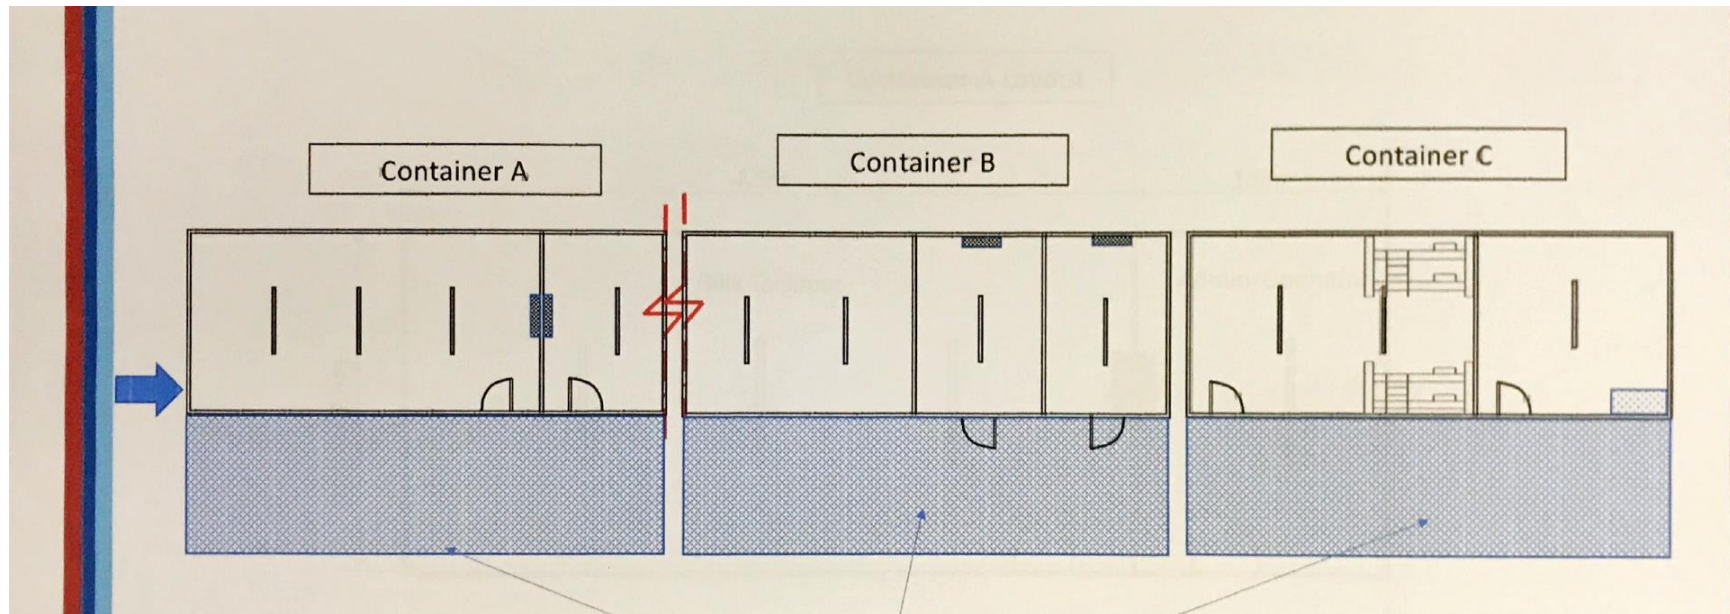

EXISTING PORTABLE CABIN LAYOUT AT JKED SG TUJOH


APPENDIX 3

JPPK / SH / 05 / 2026 – 2027

Dismantling Works, Transporting And Installation Of Three (3) Units Portable Cabins At Jabatan Kastam Dan Eksais Diraja (Jked) Building, Sungai Tujoh To Kg Bebuloh, Kampung Junjongan And Kampung Lumapas




**NEW LOCATION FOR PORTABLE CABIN/CONTAINER A :
AT KAMPUNG BEBULOH (ONE (1) UNIT)**

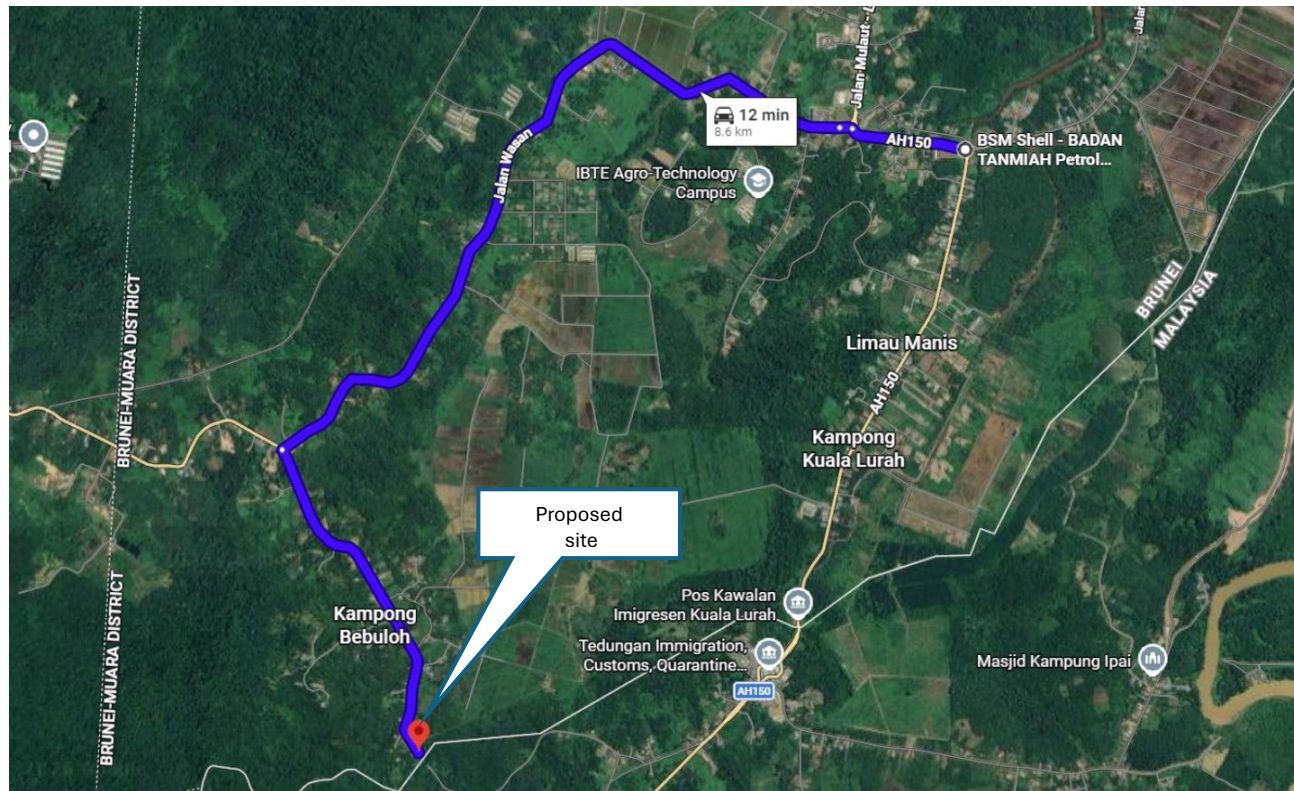

**GOOGLE MAP OF NEW LOCATION FOR PORTABLE CABIN/CONTAINER A :
AT KAMPUNG BEBULOH (ONE (1) UNIT)**

LINK:

https://www.google.com/maps/dir/4.7682266,114.8234106/4.7326966,114.7910903/@4.7511982,114.7861097,5389m/data=!3m1!1e3!4m2!4m1!3e0?entry=tту&g_ep=EgoyMDI2MDkyMi4wIKXMDSOASAFQAw%3D%3D

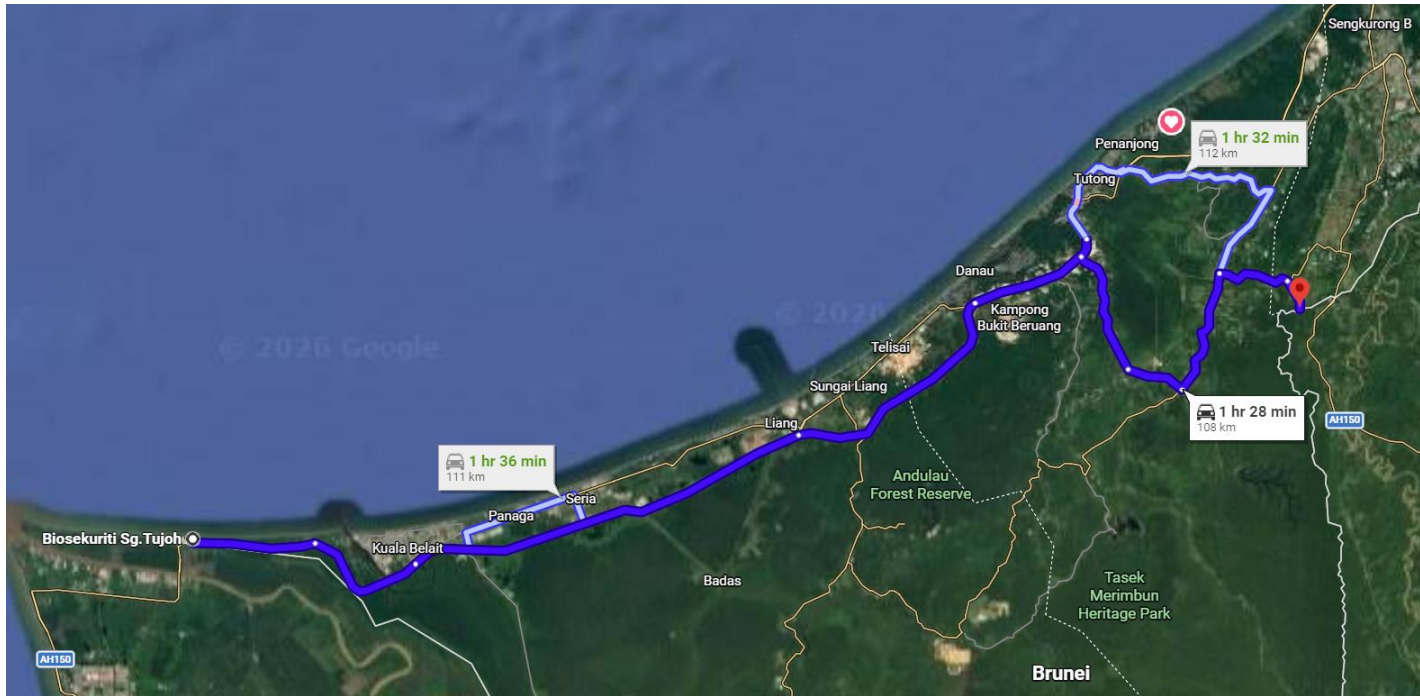

**DISTANCE FROM JKED SUNGAI TUJOH TO NEW LOCATION FOR PORTABLE CABIN/CONTAINER A :
AT KAMPUNG BEBULOH (ONE (1) UNIT)**


JPPK / SH / 05 / 2026 – 2027

Dismantling Works, Transporting And Installation Of Three (3) Units Portable Cabins At Jabatan Kastam Dan Eksais Diraja (Jked) Building, Sungai Tujoh To Kg Bebuloh, Kampung Junjongan And Kampung Lumapas



SITE LOCATION PLAN


**NEW LOCATION FOR PORTABLE CABIN/CONTAINER B :
AT KAMPUNG JUNJONGAN (ONE (1) UNIT)**

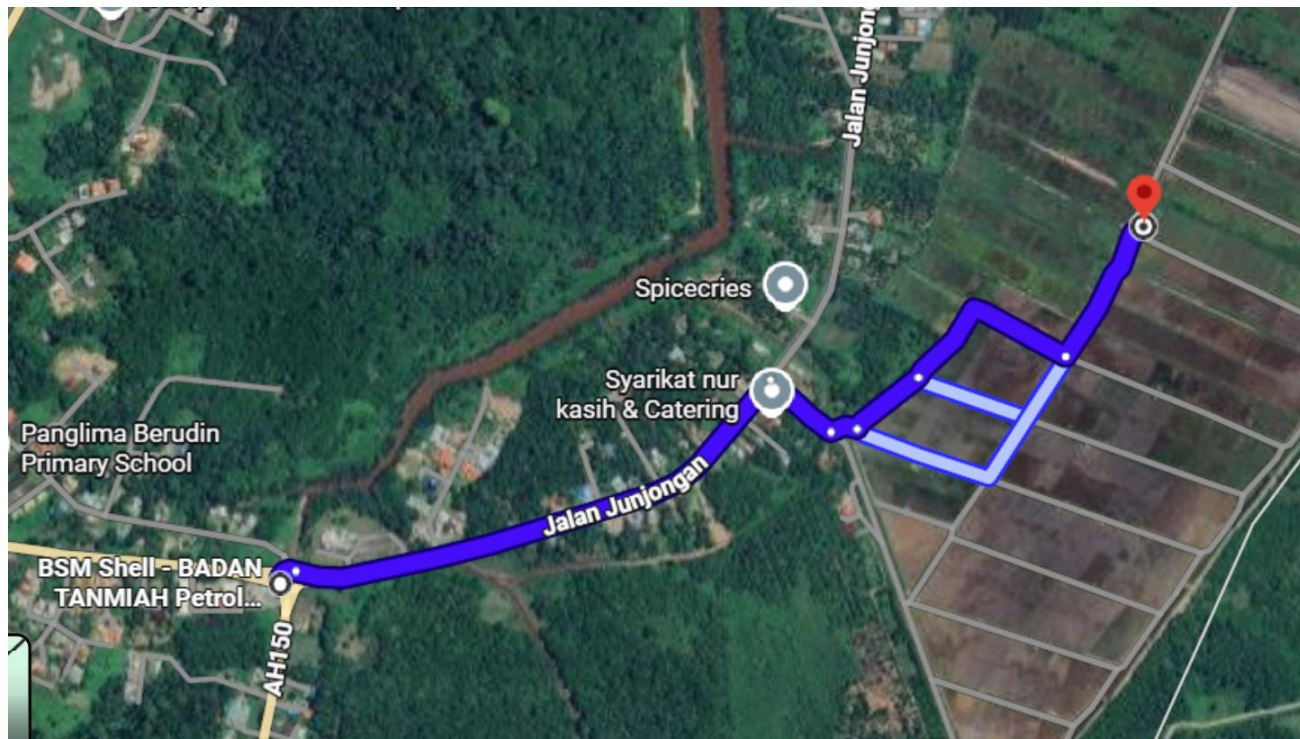

**GOOGLE MAP OF NEW LOCATION FOR PORTABLE CABIN/CONTAINER B :
AT KAMPUNG JUNJONGAN (ONE (1) UNIT)**

LINK:

https://www.google.com/maps/dir/4.7682266,114.8234106/4.7746411,114.8390086/@4.7762372,114.8414738,2728m/data=!3m1!1e3!4m2!4m1!3e0?entry=tту&g_ep=EgoyMDI2MDkyMS4wIKXMDSOASAFQAw%3D%3D

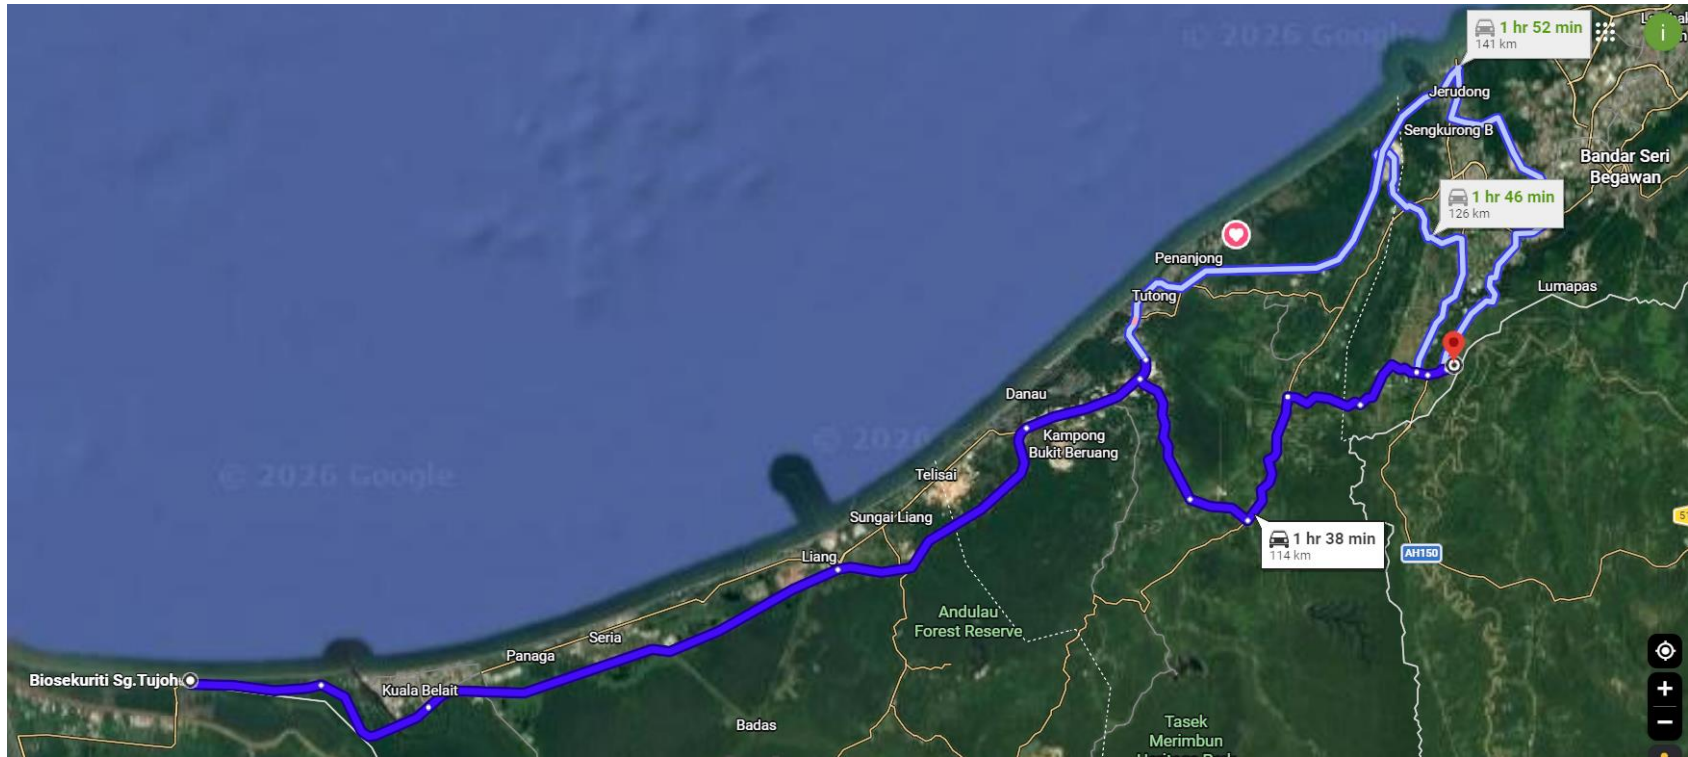


**DISTANCE FROM JKED SUNGAI TUJOH TO NEW LOCATION FOR PORTABLE CABIN/CONTAINER B :
AT KAMPUNG JUNJONGAN (ONE (1) UNIT)**

JPPK / SH / 05 / 2026 – 2027

Dismantling Works, Transporting And Installation Of Three (3) Units Portable Cabins At Jabatan Kastam Dan Eksais Diraja (Jked) Building, Sungai Tujoh To Kg Bebuloh, Kampung Junjongan And Kampung Lumapas




**NEW LOCATION FOR PORTABLE CABIN/CONTAINER C :
AT KAMPUNG LUMAPAS (ONE (1) UNIT)**

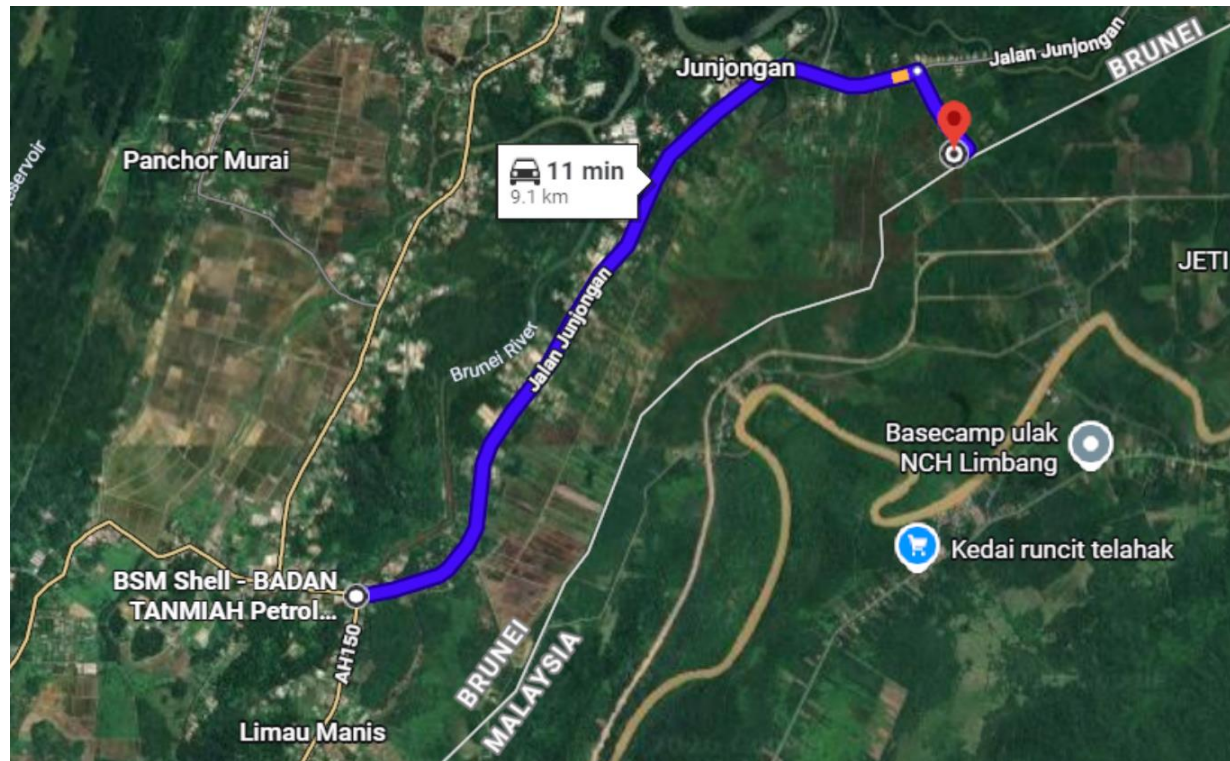

**GOOGLE MAP OF NEW LOCATION FOR PORTABLE CABIN/CONTAINER C :
AT KAMPUNG LUMAPAS (ONE (1) UNIT)**

LINK:

https://www.google.com/maps/dir/4.7682266,114.8234106/4.8053166,114.8737342/@4.7793033,114.8143129,12730m/data=!3m1!1e3!4m2!4m1!3e0?entry=tu&g_ep=EgoyMDI2MDkyMS4wIKXMDSOASAFQAw%3D%3D

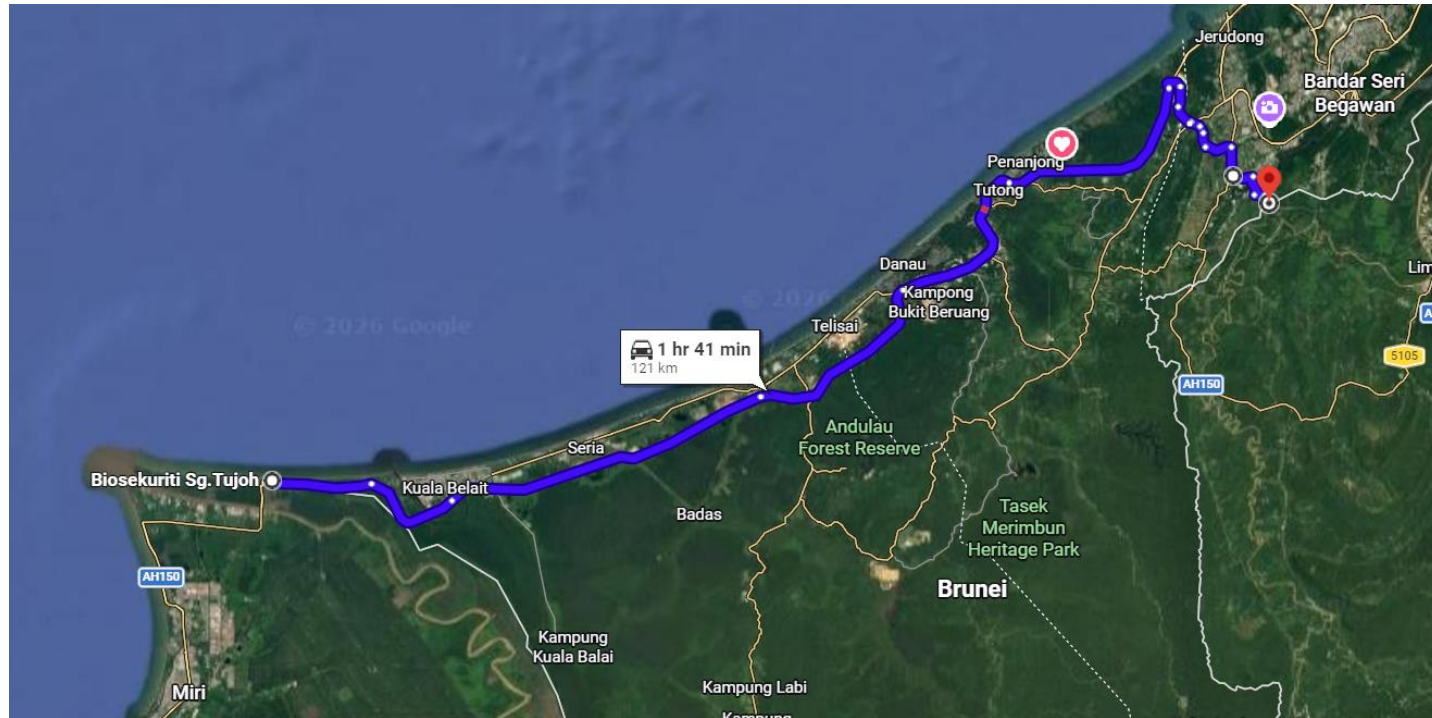

**DISTANCE FROM JKED SUNGAI TUJOH TO LOCATION FOR PORTABLE CABIN/CONTAINER C :
AT KAMPUNG LUMAPAS (ONE (1) UNIT)**
